

Red Wing Avenue Street & Utility Improvements

October 29, 2020

(Red Wing Ave, 4th St, Alley)

Project Scope:

- Street Reconstruction
- Sidewalk Replacement
- Storm Sewer
- Sanitary Sewer
- Watermain

Schedule:

Start:


April 2020

Substantial Completion:

~~October 31~~ Mid-November, 2020

Final Completion:

June 26, 2021



City Kenyon

709 2nd Street

Kenyon, MN 55946

Mark Vahlsing, City Administrator

Contractor:

Wencl Construction

Owatonna, MN

Engineer:

Bolton & Menk, Inc.

2900 43rd Street NW

Suite 100

Rochester, MN 55901

Phone: (507) 208-4332

Fax: (507) 208-4155

www.bolton-menk.com

Jordan Pankonin, EIT

Primary Resident Contact

Resident Project Representative

Cell: (507) 735-2742

jordan.pankonin@bolton-menk.com

Derek Olinger, P.E.

Project Manager

Cell: (507) 525-2685

derek.olinger@bolton-menk.com



Project Update

Paving

The contractor plans to prepare the road base for paving early next week, and pave as soon as it is ready. Please plan to park on side streets from Monday - Friday next week. During paving operations, do not drive on the new pavement for 24 hours to allow it to fully cool. Exercise caution when walking around recently paved areas, it may be very hot and could cause injury.

Concrete

The concrete work needed to get the road paved has been completed. After paving is complete, concrete work will continue on driveways and sidewalks. Please avoid walking on new concrete for 24 hours after placement. Avoid driving on concrete for 7 days.

As paving and concrete work finish up, the contractor will continue to clean up front yards and boulevards and begin working on final tasks before winter. The final top layer of pavement will be paved next year when temperatures are warm enough, as originally scheduled. Final work on seeding will also take place next year.



Sign up for email or text updates!

The project team will be sending out regular updates via email/text blast. To sign up to receive weekly email or text message notifications, please visit the project website and enter in your preferred contact information.


www.bolton-menk.com/kenyon2019



Contacts

If you have questions or concerns at any time, please contact Jordan Pankonin at (507) 735-2742, or jordan.pankonin@bolton-menk.com.

Contacting Jordan is most often the quickest means of answering questions and addressing concerns related to the project.

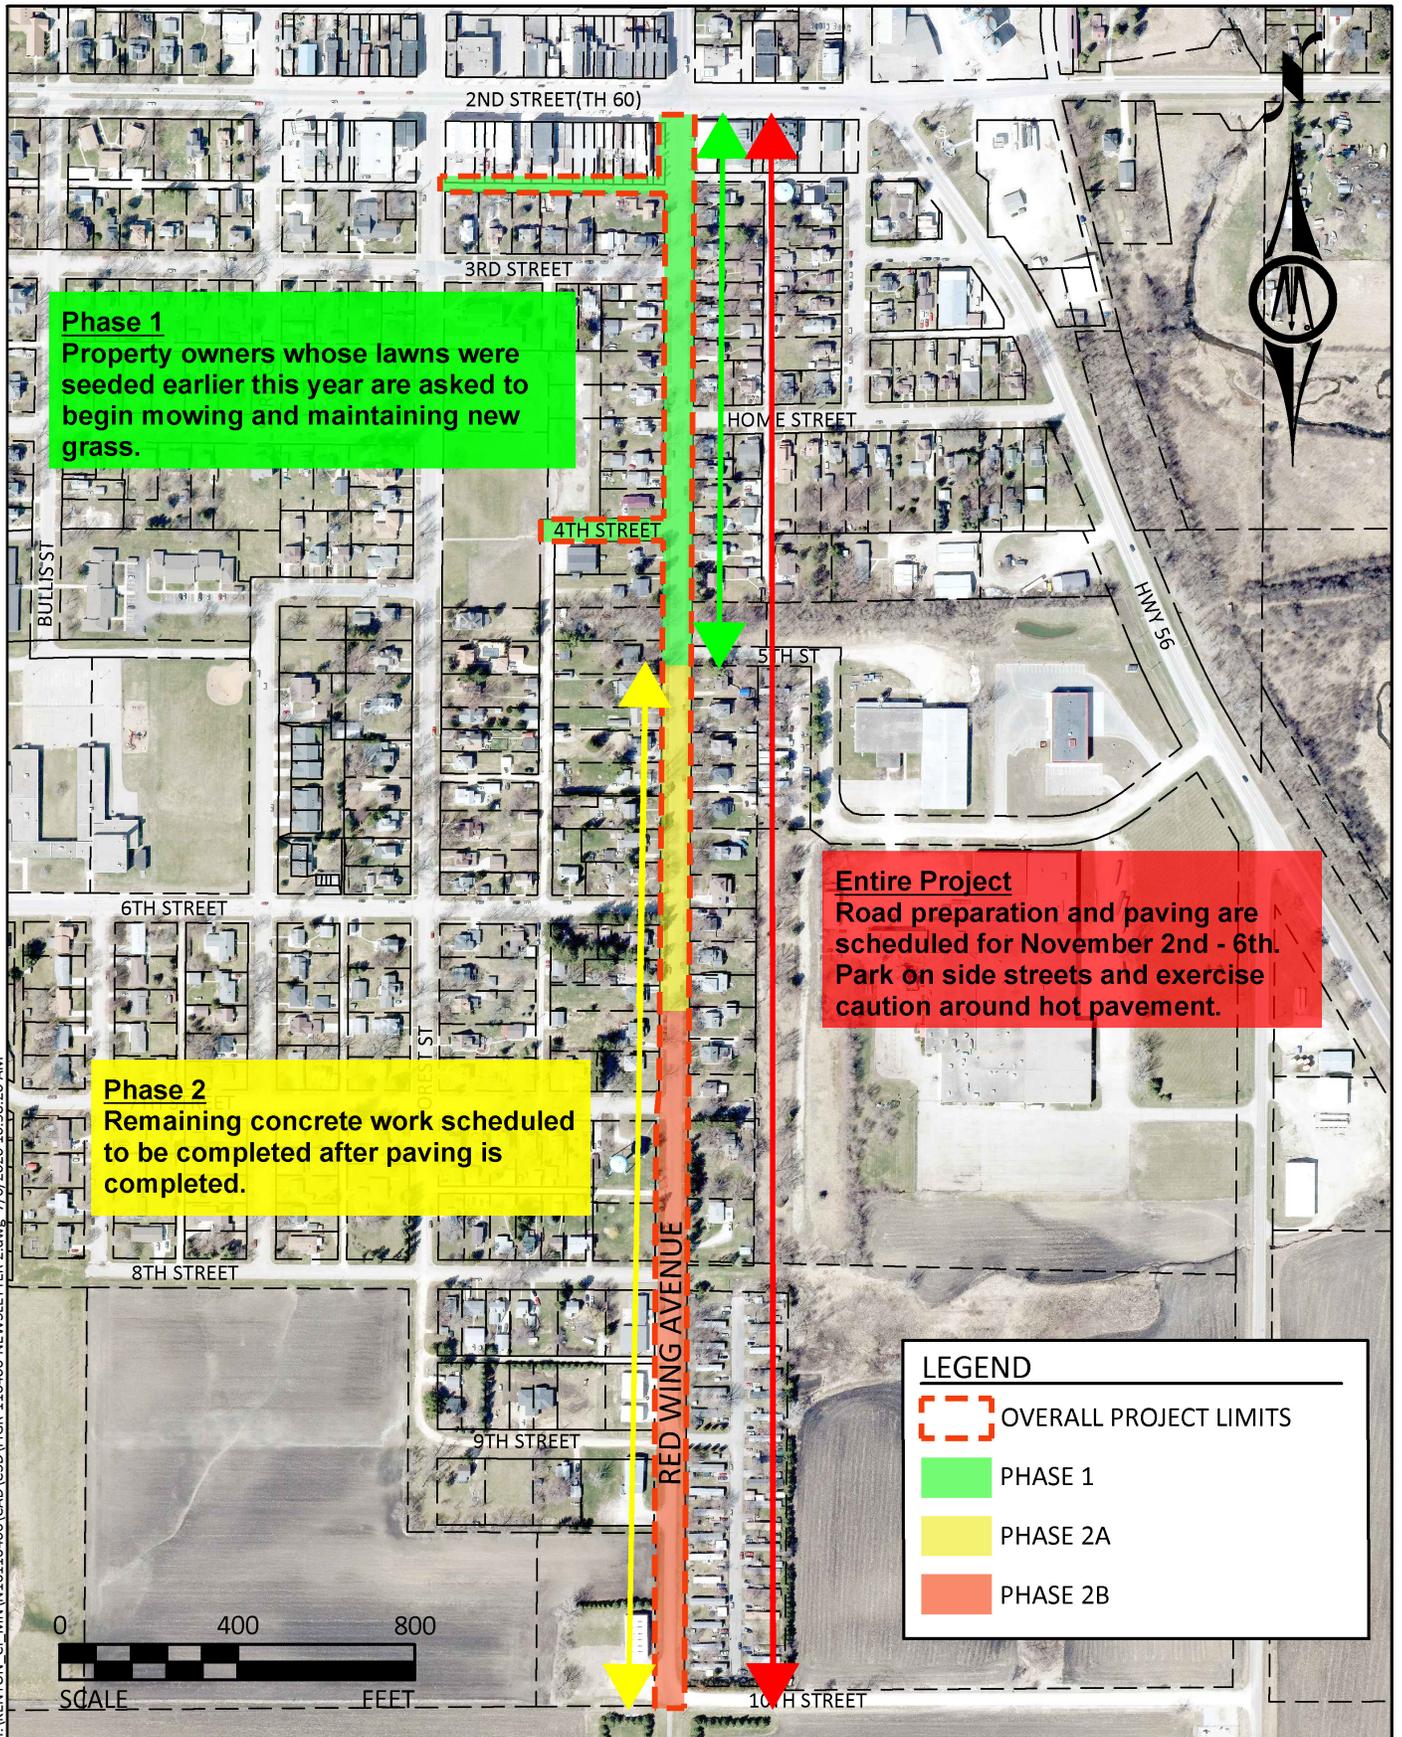

Phase 1
Property owners whose lawns were seeded earlier this year are asked to begin mowing and maintaining new grass.

Entire Project
Road preparation and paving are scheduled for November 2nd - 6th. Park on side streets and exercise caution around hot pavement.

Phase 2
Remaining concrete work scheduled to be completed after paving is completed.

LEGEND

- OVERALL PROJECT LIMITS
- PHASE 1
- PHASE 2A
- PHASE 2B

H:\KENYON_CI_MN\M16116406\CAD\C3D\FIGR-116406-NEWSLETTER 2.dwg 7/6/2020 10:58:20 AM
